



**CITY OF MARTINEZ**

**CITY COUNCIL AGENDA  
November 5, 2014**

**TO:** Mayor and City Council  
**FROM:** Don Salts, Deputy Public Works Director  
**SUBJECT:** Bus Stop Improvement Project  
**DATE:** October 29, 2014

**RECOMMENDATION:**

Adopt a resolution accepting the Bus Stop Improvement Project (C6010) per contract documents and instructing the City Clerk to file a Notice of Completion.

**BACKGROUND**

On November 6, 2013 the City Council awarded a construction contract to ABSL Construction for construction of the Bus Stop Improvement Project for a base bid amount of \$62,824.75. The project was a collaborative project between the City of Martinez and County Connection. It was funded with County Connection’s Proposition 1B funds and City Gas Tax funds. In general, the work included construction of site improvements to upgrade eight bus stop locations throughout the City of Martinez to improve access, comfort and safety to passengers using the County Connection bus service. The work included installing curb, gutter, sidewalk, benches, trash receptacles and signs; removal of tree stumps, demolishing and removal of existing sidewalk, minor grading and other associated work necessary to complete project. The final cost of the improvements was \$69,948.50.

Below is a summary of the Contact Change Order. Funding for the Change Orders came from the project contingency.

CO#1	Removal of Concrete & forming work due to unforeseen conditions	800.00
------	---	--------

The Contractor has submitted the Contractor Guarantee and the Maintenance Bond, and agrees to correct any defects as per specifications for a one-year period.

**FISCAL IMPACT:**

The project was completed within the approved budget.

**ACTION:**

Motion adopting a resolution accepting the Bus Stop improvement Project as complete and instructing the City Clerk to file a Notice of Completion.

Attachment: Site Plan

**APPROVED BY:**   
Interim City Manager

RESOLUTION NO. -14

ACCEPTING THE BUS STOP IMPROVEMENT PROJECT PER CONTRACT  
DOCUMENTS AND INSTRUCTING THE CITY CLERK TO  
FILE A NOTICE OF COMPLETION

**WHEREAS**, the City of Martinez has heretofore entered into a contract with ABSL Construction for certain work on the Project and the Public Works Director has recommended acceptance of said work of improvement as completed in accordance with plans, specifications and approved change orders and correction lists, and in accordance with the final inspection of the Deputy Director of Public Works.

**NOW, THEREFORE, BE IT RESOLVED**, by the City Council of Martinez that said work is hereby accepted as completed on this 5th day of November 2014.

**BE IT FURTHER RESOLVED** that the City Clerk, is hereby directed to file a Notice of Completion on said project.

\* \* \* \* \*


**I HEREBY CERTIFY** that the foregoing is a true and correct copy of a resolution duly adopted by the City Council of the City of Martinez at a Regular Meeting of said Council held on the 5th day of November, 2014, by the following vote:

AYES:

NOES:

ABSENT:

RICHARD G. HERNANDEZ, CITY CLERK  
CITY OF MARTINEZ

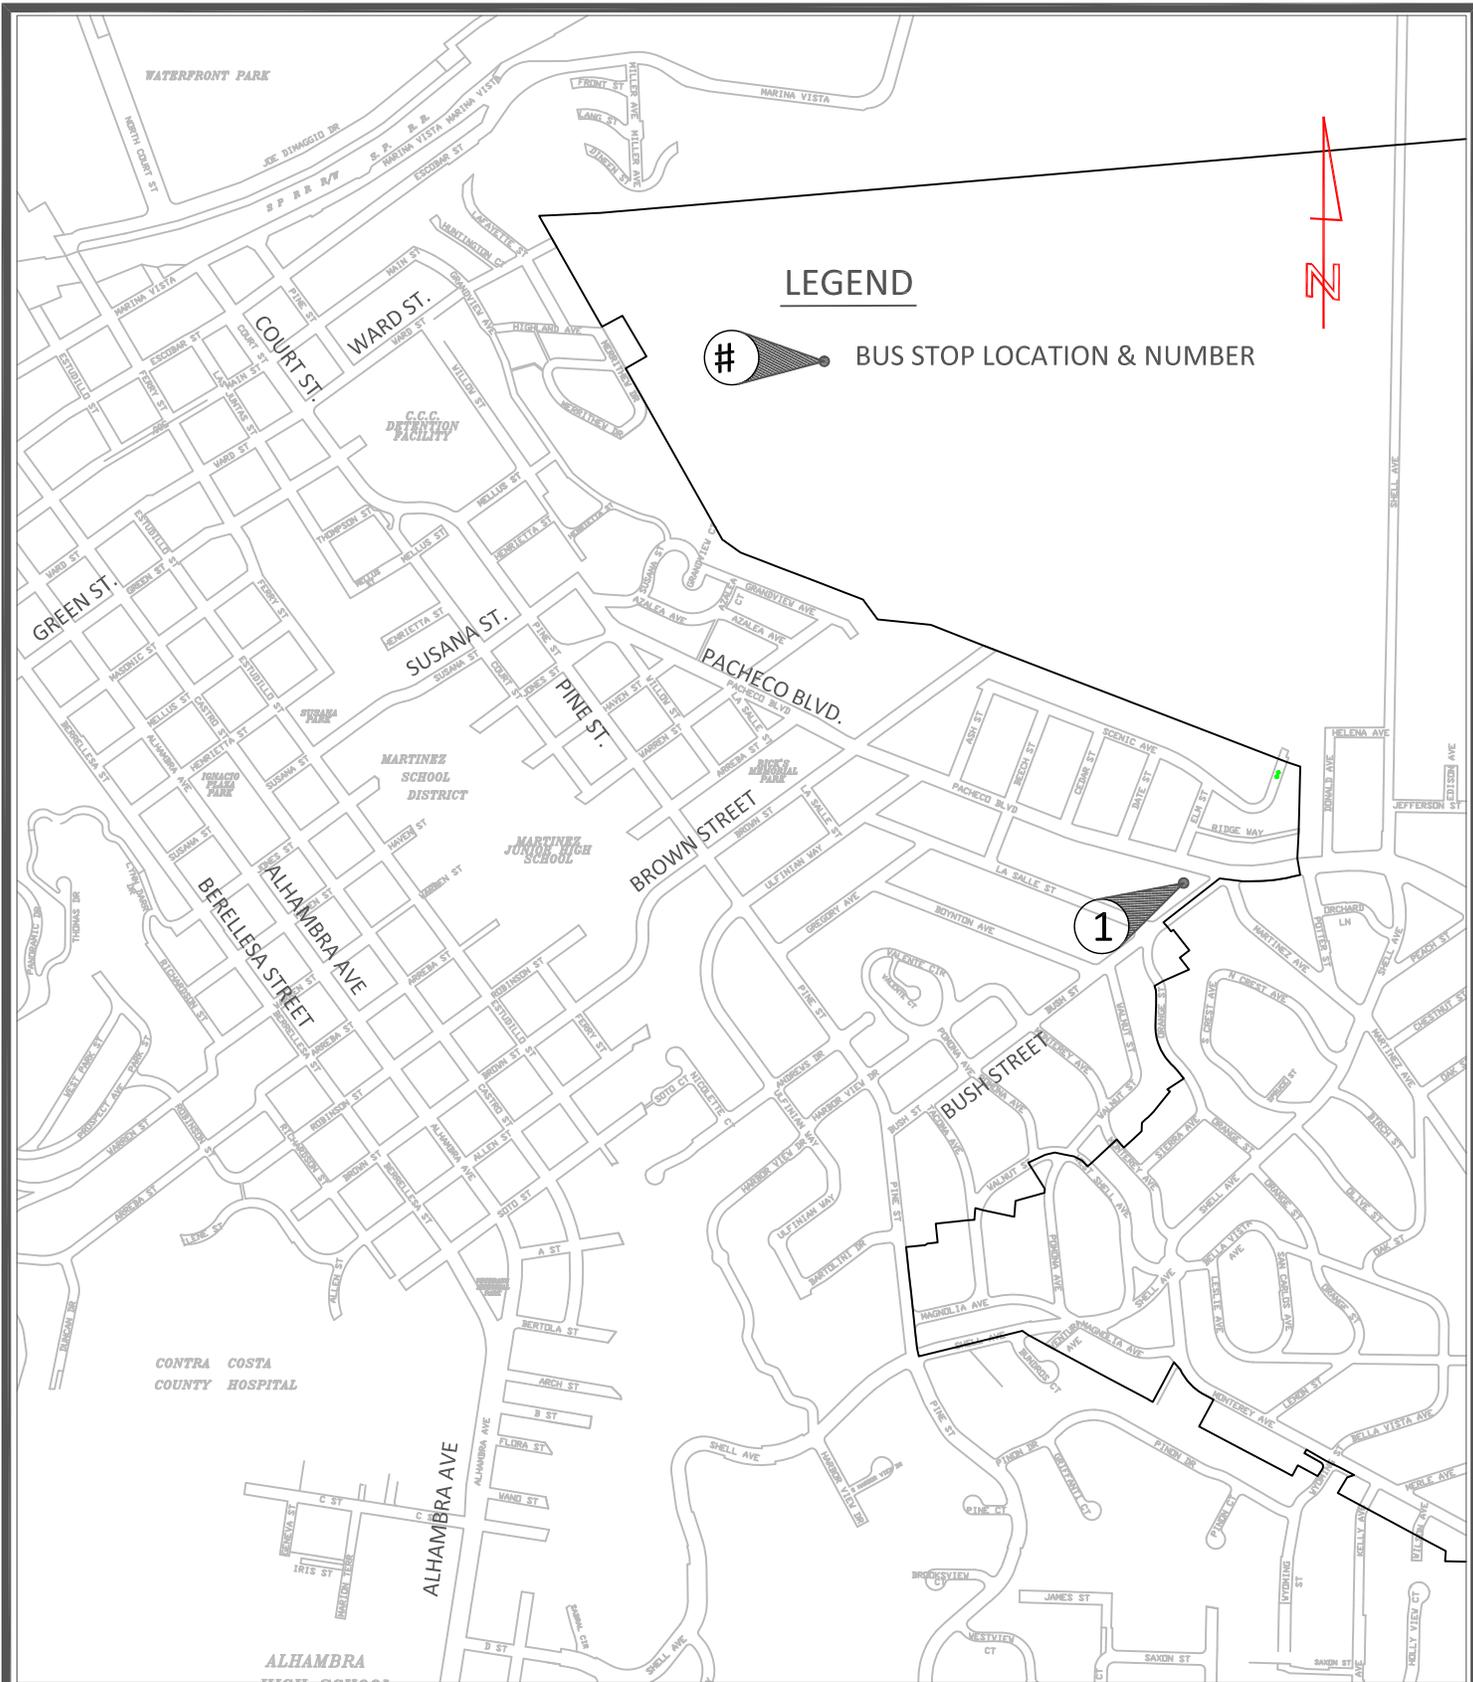

VICINITY MAP  
 CITY OF MARTINEZ  
 BUS STOP IMPROVEMENT PROJECT

DATE: 4/9/2013


SCALE: NONE

SHEET

2

OF 17



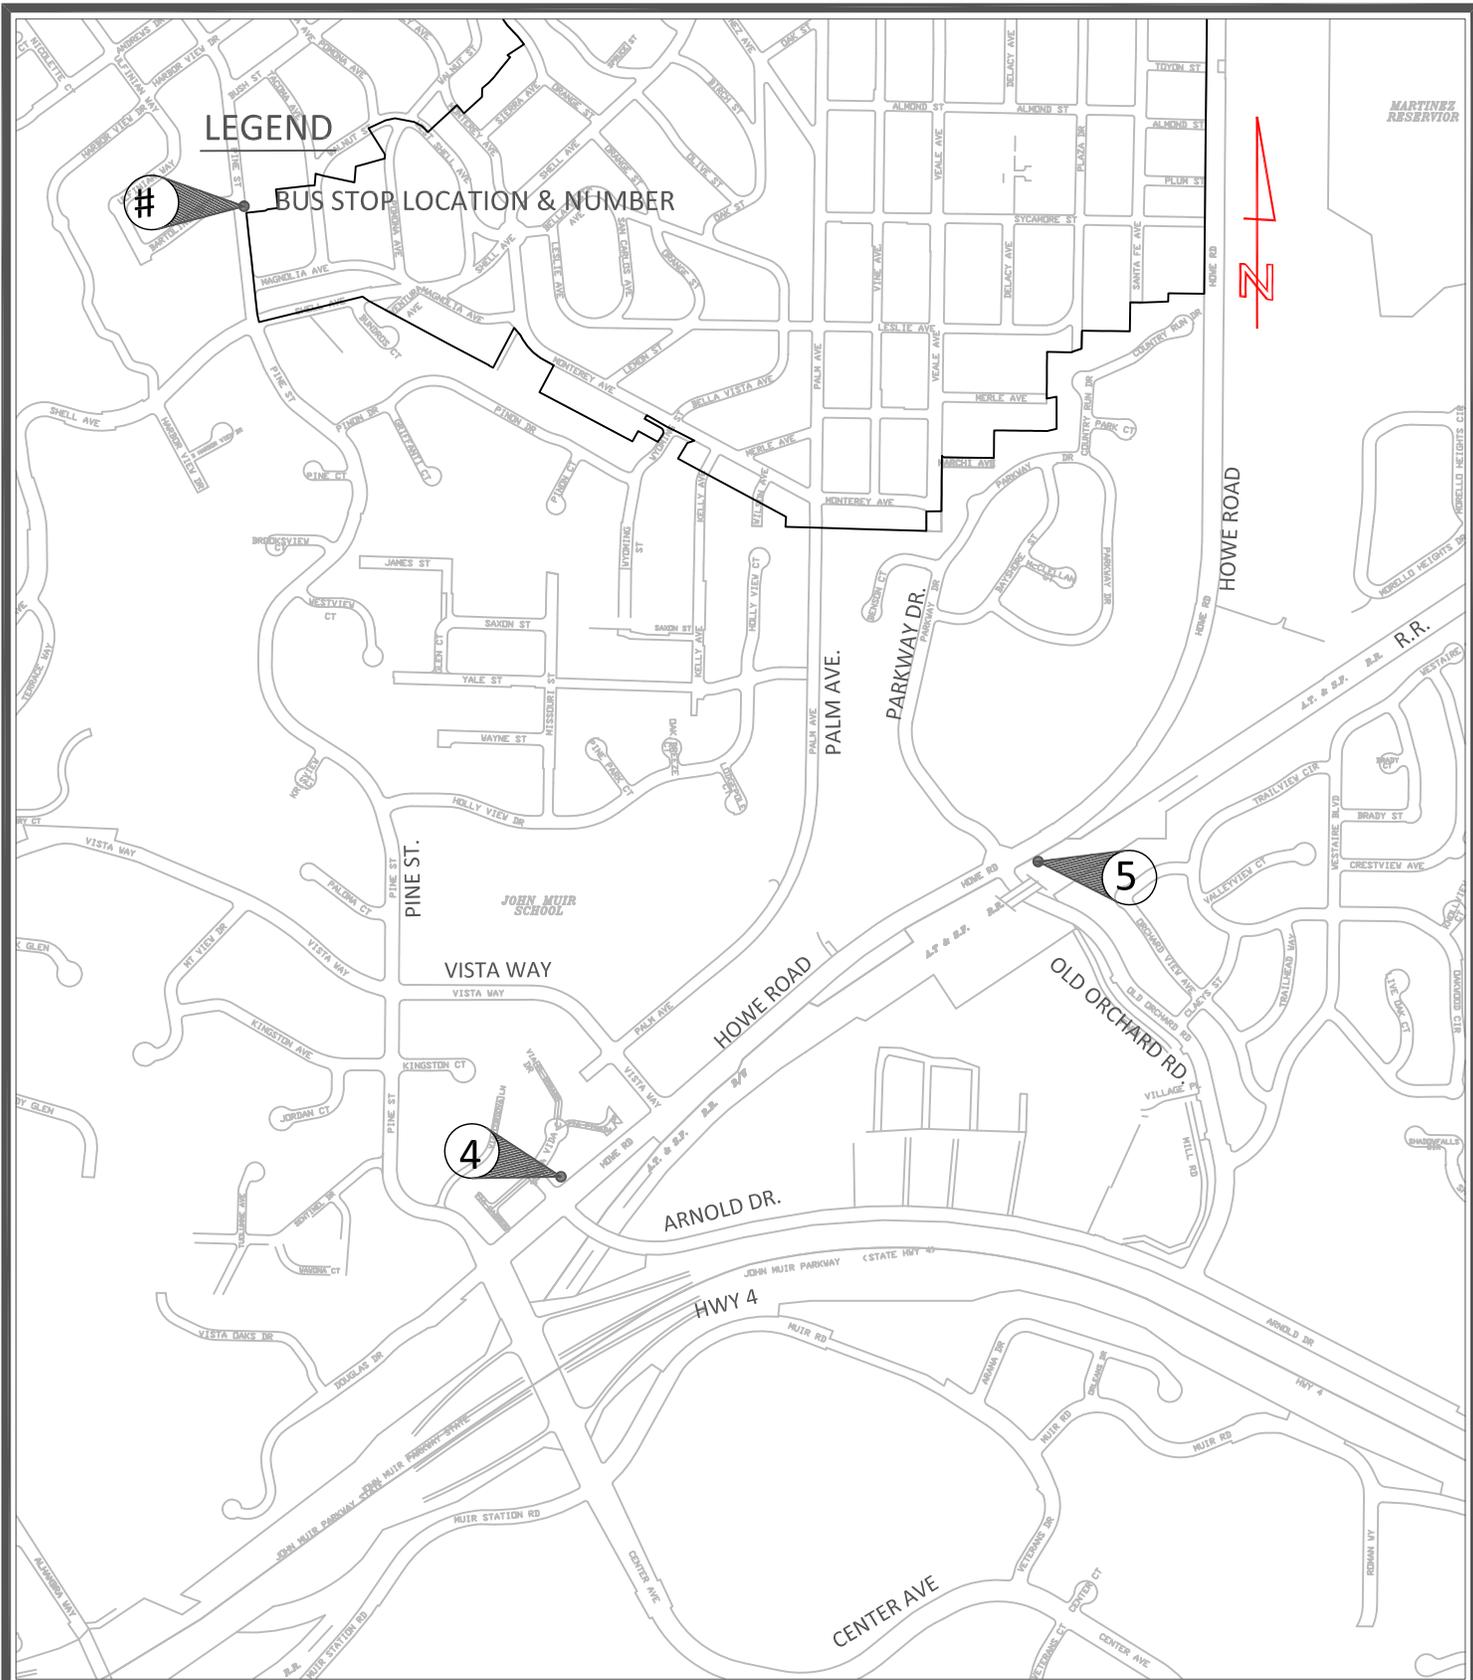

**VICINITY MAP**  
**CITY OF MARTINEZ**  
**BUS STOP IMPROVEMENT PROJECT**

DATE: 4/9/2013

SCALE: NONE

SHEET

**4**

OF 17

